
Agile Workshop

Ways of Working

February 12, 2025



Izabela Oślizło-Fizia

www.linkedin.com/in/izaosl



Technology Program Manager
Delivery Manager
2023 - present



Scaled Regulatory Ops Manager
Project Manager, IP Operations
IP Specialist
2016 - 2022



MSc, Management
2014 - 2016



BA, Business English
2010 - 2013



Project Management Professional (PMP)
2020



1. Agenda

- Kick off
- Project Management Refresher
- Scrum and Kanban Overview
- Break
- Ways of Working
- Break
- Main Activity: Ways of Working & Working Agreement Creation
- Wrap up & Reflection

Icebreaker

- Name
- TV show you're watching right now

What is a Project?



**A temporary endeavour
undertaken to create a unique
product, service, or result.**

PMI

Defining a Project

Characteristic #1

Unique

Characteristic #2

Start and end date

Characteristic #3

Goal

Characteristic #4

Collection of tasks

Characteristic #5


Resources

Characteristic #6

Stakeholders

Project Life Cycle

(Process Groups)

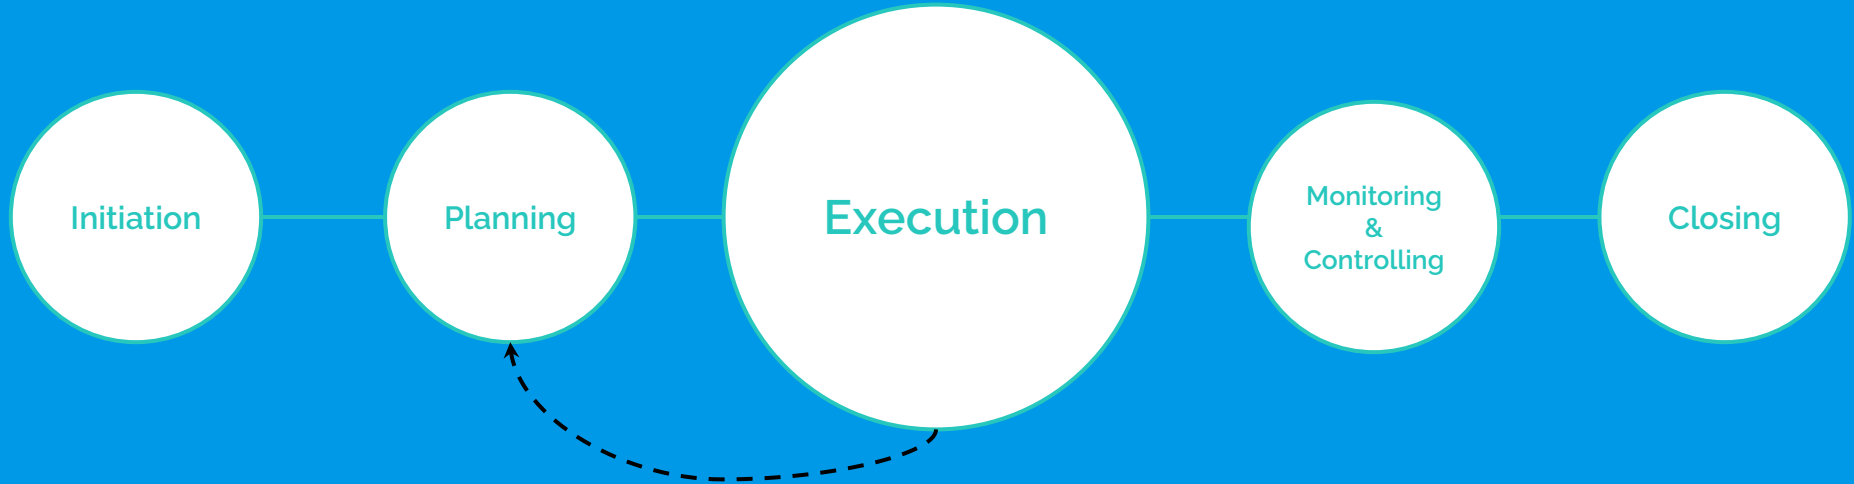

—

Think back to a project you've worked on—what was your role, and what approach did you use to manage the tasks and team?

Waterfall Methodology

Follows a linear sequential flow, with each phase dependent on the deliverables of the prior ones.

- 👍 Clear structure
- 👍 Well-documented process
- 👍 Good for projects with well-defined requirements

- 👎 Inflexible to changes
- 👎 Late detection of issues

Agile Methodology

It emphasizes flexibility and iterative progress, allowing for adjustments throughout the project.

👍 Flexible and adaptive to changes

👍 High customer involvement and satisfaction

👍 Early and continuous delivery

💡 Can lead to scope creep without proper management

💡 Less cost and timeline predictability



Agile Manifesto

Individuals and interactions over processes and tools


Working software over comprehensive documentation

Customer collaboration over contract negotiation


Responding to change over following a plan

That is, while there is value in the items on the right,
we value the items on the left more.

Agile vs. Waterfall

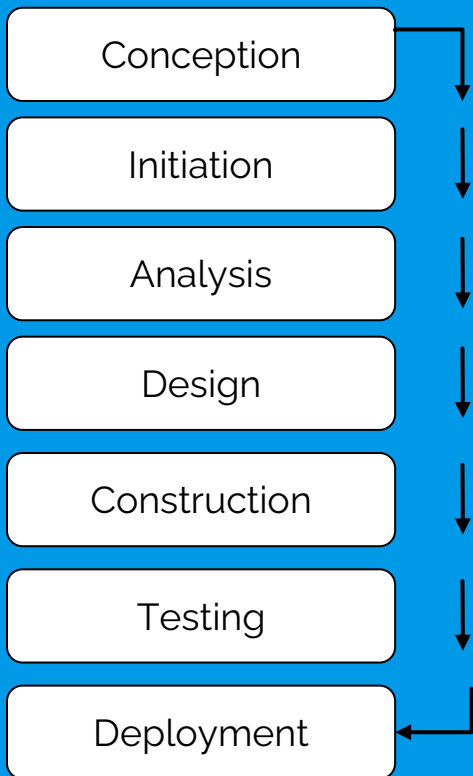

VS

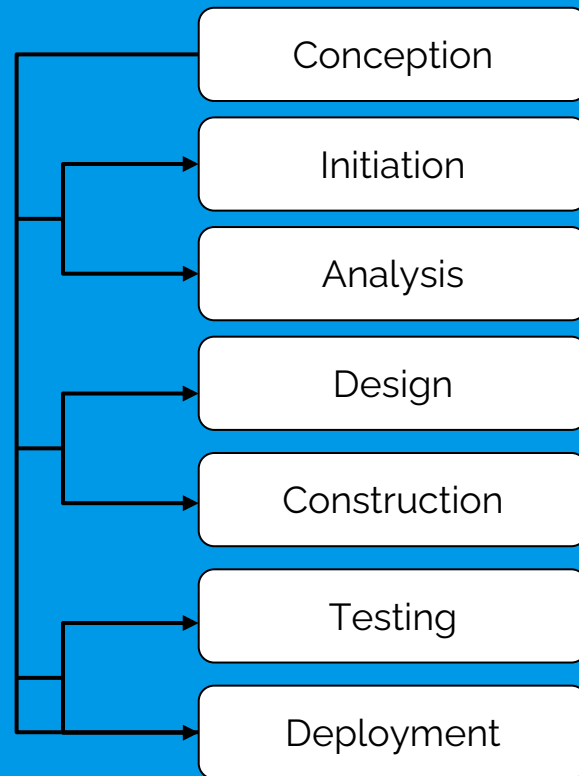



Ken Schwaber & Jeff Sutherland

The Scrum Guide

The Definitive Guide to Scrum: The Rules of the Game



**You learn Agile in 2 weeks, but
master it an entire life.**

Scrum vs kanban

The Scrum Framework



Scrum Events Quick Reference

The following is a quick summary of the timeboxed Scrum events. The Sprint is a container for all of these events and is required to have a maximum duration of one month or less.

Event	Inspection	Adaptation	Participants	Timebox
Sprint Planning	Product Backlog, Product Goal, Definition of Done	Sprint Backlog, Sprint Goal	Scrum Team	8 hours for a 1 month Sprint
Daily Scrum	Progress toward Sprint Goal	Sprint Backlog	Developers	15 minutes
Sprint Review	Increment, Sprint, Product Backlog, Progress toward Product Goal	Product Backlog	Scrum Team, Stakeholders	4 hours for a 1 month Sprint
Sprint Retrospective	Sprint, Definition of Done	Actionable improvements, Definition of Done	Scrum Team	3 hours for a 1 month Sprint

Sprint Planning

1 hr/ sprint

Daily Scrum (Stand up)

15 min daily

Sprint Review

1hr/ 1-2 sprints

Sprint Retrospective

1hr/ sprint

Refinement (Backlog Grooming)

1hr/ sprint

Jira

Your work

Projects

Filter

Dashboards

Teams

Plans

Apps

Create

Search

Beyond Gravity

Software project

PLANNING

Timeline

Backlog

Board

Reports

Issues

DEVELOPMENT

Code

Security

Releases

OPERATIONS

Deployments

Incidents BETA

On-call

Project Pages

Add shortcut

Project settings

You're in a team-managed project

Learn more

Projects

Beyond Gravity

Backlog

+3

Epic

Label

Type

Insights

View settings

Sprint 3: 7 Feb - 21 Feb (8 issues)

Complete sprint

NUC-344 Optimize experience for mobile ...

IN PROGRESS

2

NUC-360 Onboard workout options (OWO)

TO DO

1

NUC-337 Multi-deet search UI mobile web

TO DO

5

NUC-339 Billing system integration

TO DO

3

NUC-340 Account settings defaults

IN PROGRESS

4

NUC-341 Quick payment

IN PROGRESS

2

NUC-342 Fast trip search

TO DO

1

NUC-335 Affiliate links integration - frontend

IN PROGRESS

2

Create issue

Sprint 4: 22 Feb - 7 Mar (4 issues)

Complete sprint

NUC-336 Quick booking for accommodations

TO DO

1

NUC-346 Adapt web app payments provider

TO DO

2

NUC-343 Fluid booking on tablets

TO DO

3

NUC-354 Shopping cart purchasing error

TO DO

4

Create issue

NUC-378

NUC-346

Adapt web app no new payments provider

To Do

Actions

Description

As an employee I'd need to understand the rules and regulations of Beyond Gravity while working at the company on Mars. In general, rules should be the same as they are on Earth unless local rules on Mars prohibit otherwise. Please file any discrepancies in Jira so that we can review them and make decisions that work for our Martian colleagues.

Details

Assignee

Aliza Wilson

Assign to me

Labels

None

Sprint

Sprint 2

Priority

Lowest

Story Points

2

Release

None

Development

Create branch

Board



Epic ▾



4 days remaining

Complete sprint



GROUP BY

Choices ▾

TO DO · 12

Implement feedback collector

NUC-205

9



Bump version for new API for billing

NUC-206

3



Add NPS feedback to wallboard

NUC-208

1



IN PROGRESS · 4

Update T&C copy with v1.9 from the writers guild in all products that have cross country compliance

NUC-213



1



Tech spike on new stripe integration with paypal

NUC-215

3



Refactor stripe verification key validator to a single call to avoid timing out on slow connections

NUC-216

3



Change phone number field type to 'phone'

NUC-217



1



IN REVIEW · 4

Multi-dest search UI web

NUC-338

5



DONE · 4

Quick booking for accommodations - web

NUC-336



4



Adapt web app no new payments provider

NUC-346



3



Fluid booking on tablets

NUC-343



5



Shopping cart purchasing error - quick fix required.

NUC-354



1



Definition of Ready

DoR: This is the criteria to determine if a task or user story is ready for a team to tackle

E.g.:

- The user story has a clear description and well-defined acceptance criteria
- All dependencies are identified and resolved
- The story is estimated and small enough to be completed within a sprint

Definition of Done

DoD: This is the benchmark to evaluate when a task or user story is complete

E.g.:

- Code is committed, reviewed, and merged
- Automated and manual tests are passed
- Documentation is updated if necessary



Break



THE AGILE COACH

WHAT IS KANBAN?

Beyond Gravity
Software project

PLANNING

Roadmap

Backlog

Board

Reports

Issues

DEVELOPMENT

Code

Security

Releases

Project settings

Projects / Beyond Gravity

Board

Search



Epic ▾

GROUP BY

None ▾

Insights

TO DO 0

Optimize experience for mobile web

BILLING

NUC-344



Onboard workout options (OWO)

ACCOUNTS

NUC-360



Multi-dest search UI mobileweb

ACCOUNTS

NUC-337



Billing system integration - frontend

FORMS

NUC-338



Account settings defaults

ACCOUNTS

NUC-340



IN PROGRESS 0

Fast trip search

ACCOUNTS

NUC-342



Affelife links integration - frontend

BILLING

NUC-335



Shopping cart purchasing error - quick fix required

FORMS

NUC-341



IN REVIEW 0

Revise and streamline booking flow

ACCOUNTS

NUC-367



Travel suggestion experiments

ACCOUNTS

NUC-358



Ongoing customer satisfaction

ACCOUNTS

NUC-354



Planet Taxi Device exploration & research

FEEDBACK

NUC-351



DONE ✓ 0

High outage: Software bug fix - BG Web-store app crashing

BILLING

NUC-340



Web-store purchasing performance issue fix....t

FORMS


NUC-341






Work in Progress Limits (WIP)

- Sets the maximum number of tasks that can be worked on simultaneously at any given stage of a workflow.
- Prevents teams from overloading themselves, reduces bottlenecks, and improves focus.
- If a team sets a WIP limit of 3 in the "In Progress" column of a Kanban board, no more than three tasks can be worked on at once. A new task can only be added when one is completed.

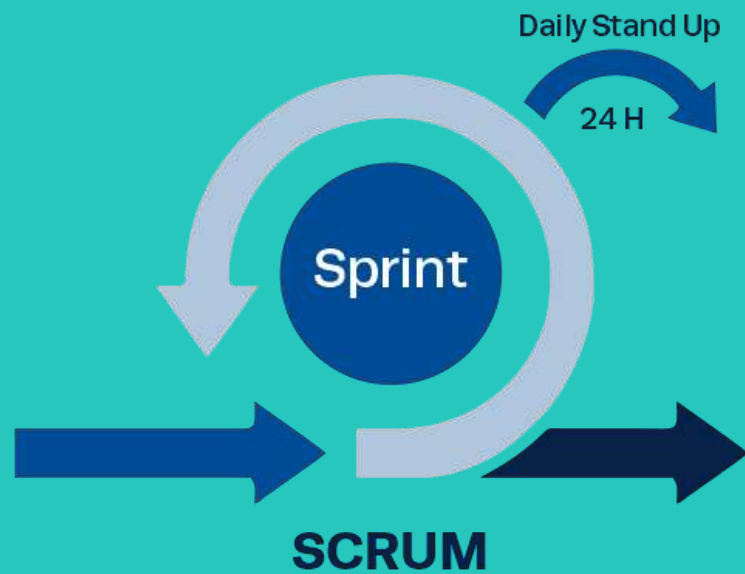

VS

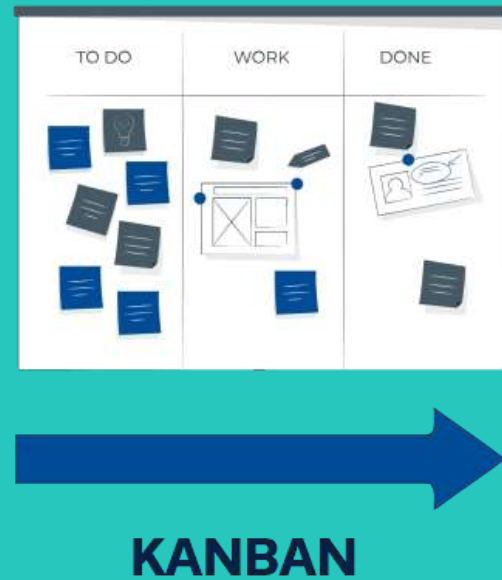

Scrum vs kanban

Aspect	Scrum (Time-Boxed)	Kanban (Flow-Based)
Sprint Planning	Every Sprint	Continuous
Daily Stand-Up	Focuses on progress toward a sprint goal	Focuses on flow efficiency
Artifacts	Product backlog, sprint backlog	Kanban board
Facilitator	Scrum Master	No dedicated role
Fixed iterations	Yes - e.g. 2-week sprints	No, work flows continuously

Developing a Mobile Banking App

Project: A fintech company is building a mobile banking app that allows users to check balances, transfer money, and pay bills. Regulatory compliance is critical, but features may evolve based on user feedback.

ANSWER

Recommended Methodology: Agile

Why?

- Customer expectations and feature requests will evolve.
- Iterative releases allow testing and improvement based on user feedback.
- Security and compliance aspects can be prioritized while still allowing flexibility in UI/UX.

Constructing a New Office Building

Project: A construction firm is building a new corporate office. The architectural design, permits, and construction phases are strictly planned, with little room for mid-project changes.

ANSWER

Recommended Methodology: Waterfall

Why?

- Each phase (design, permits, foundation, structure) must be completed in order.
- Changes mid-project could cause significant delays and cost overruns.
- The final product must be fully complete before it can be used.

Publishing an Annual Corporate Report

Project: A corporation is preparing its annual report, including financial statements, executive summaries, and market analysis. The report must be finalized and published by a fixed deadline.

ANSWER

Recommended Methodology: Waterfall

Why?

- The structure and content must be planned in advance with strict deadlines.
- Regulatory and financial accuracy is critical, leaving little room for iterative changes.
- The final report is a single deliverable, not an evolving product.

Implementing an AI Chatbot for Customer Support

Project: A company is deploying an AI chatbot to handle customer inquiries. The initial version will handle basic questions, with plans to expand its capabilities over time.

ANSWER

Recommended Methodology: Agile

Why?

- The chatbot can be launched with core functionality and improved iteratively.
- Real-world customer interactions will guide enhancements.
- Features like sentiment analysis or multi-language support can be added progressively.



How the customer explained it




How the project leader understood it



How the analyst designed it




How the programmer wrote it



What the beta testers received




How the business consultant described it




How the project was documented




What operations installed




How the customer was billed



How it was supported



iSwing



What the customer really needed

Ways of Working → Working Agreement

- Often defined at a “Sprint Zero”
 - A document that defines how the team will interact, communicate, and work together
 - It establishes norms and values that help teams work efficiently and effectively
-

Ways of Working → Working Agreement

A Working Agreement is:

- Created by and for the team
- Looks to codify behaviours and expectations for the team
- Provides a mechanism for the team to share their desired behaviours

An effective working agreement is:

- Publicly available
 - Nobody is above the contract
 - Each member of the team is present at the time of a creation of the contract and had their input and say in its creation
 - Is revisited and updated regularly
-

Working Agreement

Example 1: here

Example 2: here



Break

Activity Overview

- Handout [here](#)
 - Create 3-4 groups, 5-6 people each
 - **Your project: Organise an in-person Open Day @ Coventry University Wrocław on May 5th, 2025**
 - Each group will:
 - Prepare a brief Project Summary
 - Create a Working Agreement, inclusive of DoR, and DoD
 - Present their Working Agreement to the class
-



It's a Wrap!

- How would your past projects have benefited from a more flexible, iterative approach like Agile?
- How did the process of creating a Working Agreement change how you think about collaboration?
- Q&A & Thanks!
